



# TOWN OF BROOKLINE


*Massachusetts*

## DEPARTMENT OF PUBLIC WORKS Engineering & Transportation Division

September 27, 2011

*Andrew M. Pappastergion*  
Commissioner  
*Peter M. Ditto, PE*  
Director

### OCTOBER OVERVIEW of SEWER SEPARATION PROJECT

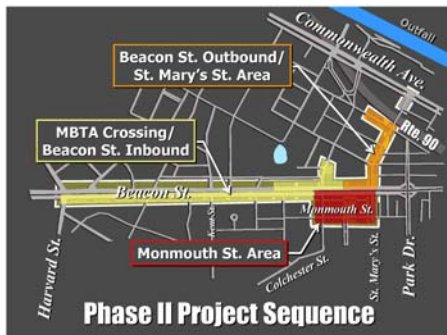

- (A) **ST. MARY'S STREET AREA**  
**October Work:** Complete utility work, backfill access pit and restore street/sidewalk at the Mountfort Street intersection; Euston and Ivy pits will remain open pending new sewer connection  
**Traffic/Parking:** St. Mary's to remain ONE-WAY southbound pending restoration of access pits
- (B) **BEACON STREET (outbound) COMMERCIAL AREA**  
**October Work:** Complete tunneling and installation of new 18" sewer pipe between St. Mary's and Carlton; Demobilize 18" drilling equipment; Install manhole and adjust utilities at St. Mary's access pit; Mobilize 48" drilling equipment at Carlton end-Oct  
**Traffic/Parking:** Vehicular travel will remain reduced to a **Single lane westbound**; **Curbside parking** will continue to be **restricted** during work day hours immediate to work sites; **Median parking** will remain **open** at all times
- (C) **BEACON STREET (inbound) AREA**  
**October Work:** Resume tunneling and installation of new 48" sewer pipe from Borland to Kent access pits; Demobilize 48" drilling equipment and relocate to Beacon/Carlton; **NationalGrid** installs new gas line and services from Carlton to St. Mary's  
**Traffic/Parking:** **Single lane** of travel eastbound from St. Paul to St. Mary's; **Curbside parking restricted** adjacent active work zones; **Borland St** to remain **closed** at Beacon
- (D) **MONMOUTH STREET AREA**  
**October Work:** At **Monmouth Street**, complete open-cut trenching and installation of new 57" sewer line; At **St. Mary's Street**, mobilize equipment/material and launch trenching operation to install new Sewer/Drain lines from Beacon south to Monmouth/Medfield  
**Traffic/Parking:** **MONMOUTH** open to **LOCAL TRAFFIC ONLY**, while **ST. MARY'S CLOSED** from Beacon south to Monmouth during **WORK HOURS**; Normal operations resume nights/weekends
- (E) **CARLTON STREET CORRIDOR**  
**October Work:** Complete new drain line installation from Beacon north through Churchill first week Oct; Anticipate mobilization at Beacon end-Oct for tunneling operation beneath MBTA tracks  
**Traffic/Parking:** No scheduled interruptions; Anticipate construction delays at Beacon end-Oct
