




Gateway East Phase 2A Construction Plan  
Beginning September 3<sup>rd</sup>, 2019

- MDR will begin by installing drainage structures, under ground electric conduit and precast light pole bases. Duration is approximately 20 days +/-
  - **Pending Approval** – MDR will establish a permanent work zone, delineated by jersey barrier, in the East Bound right lane on Washington Street. The bus stop will be moved further down towards Juniper Street – pending approval
  - Excavate & cut in new roadway and place and compact to sub grade duration is approximately 6 days +/-
  - Place Binder & Intermediate paving courses on new roadway duration is approximately 2 days +/-
  - Concrete & block retaining wall work – pending approvals
  - Install new curb and sidewalk duration is approximately 11 days +/-
  - Phase 2A remains closed to traffic & pedestrians
- 
- As soon as Phase I work, drainage and electric conduit becomes available pending design review, work will continue on Phase I
  - Prior to the crossover to phases 2B & 2C, 2A will be open to traffic. Barrier will be placed with “Right Turn Only” signage for traffic in front of Juniper and Pearl Street (on Washington St) during this phase. Juniper Street and Walnut Street will remain unchanged until 2A is opened.
- 
- Signalization for Pearl Street and Walnut Street to be completed prior to beginning of phase 3

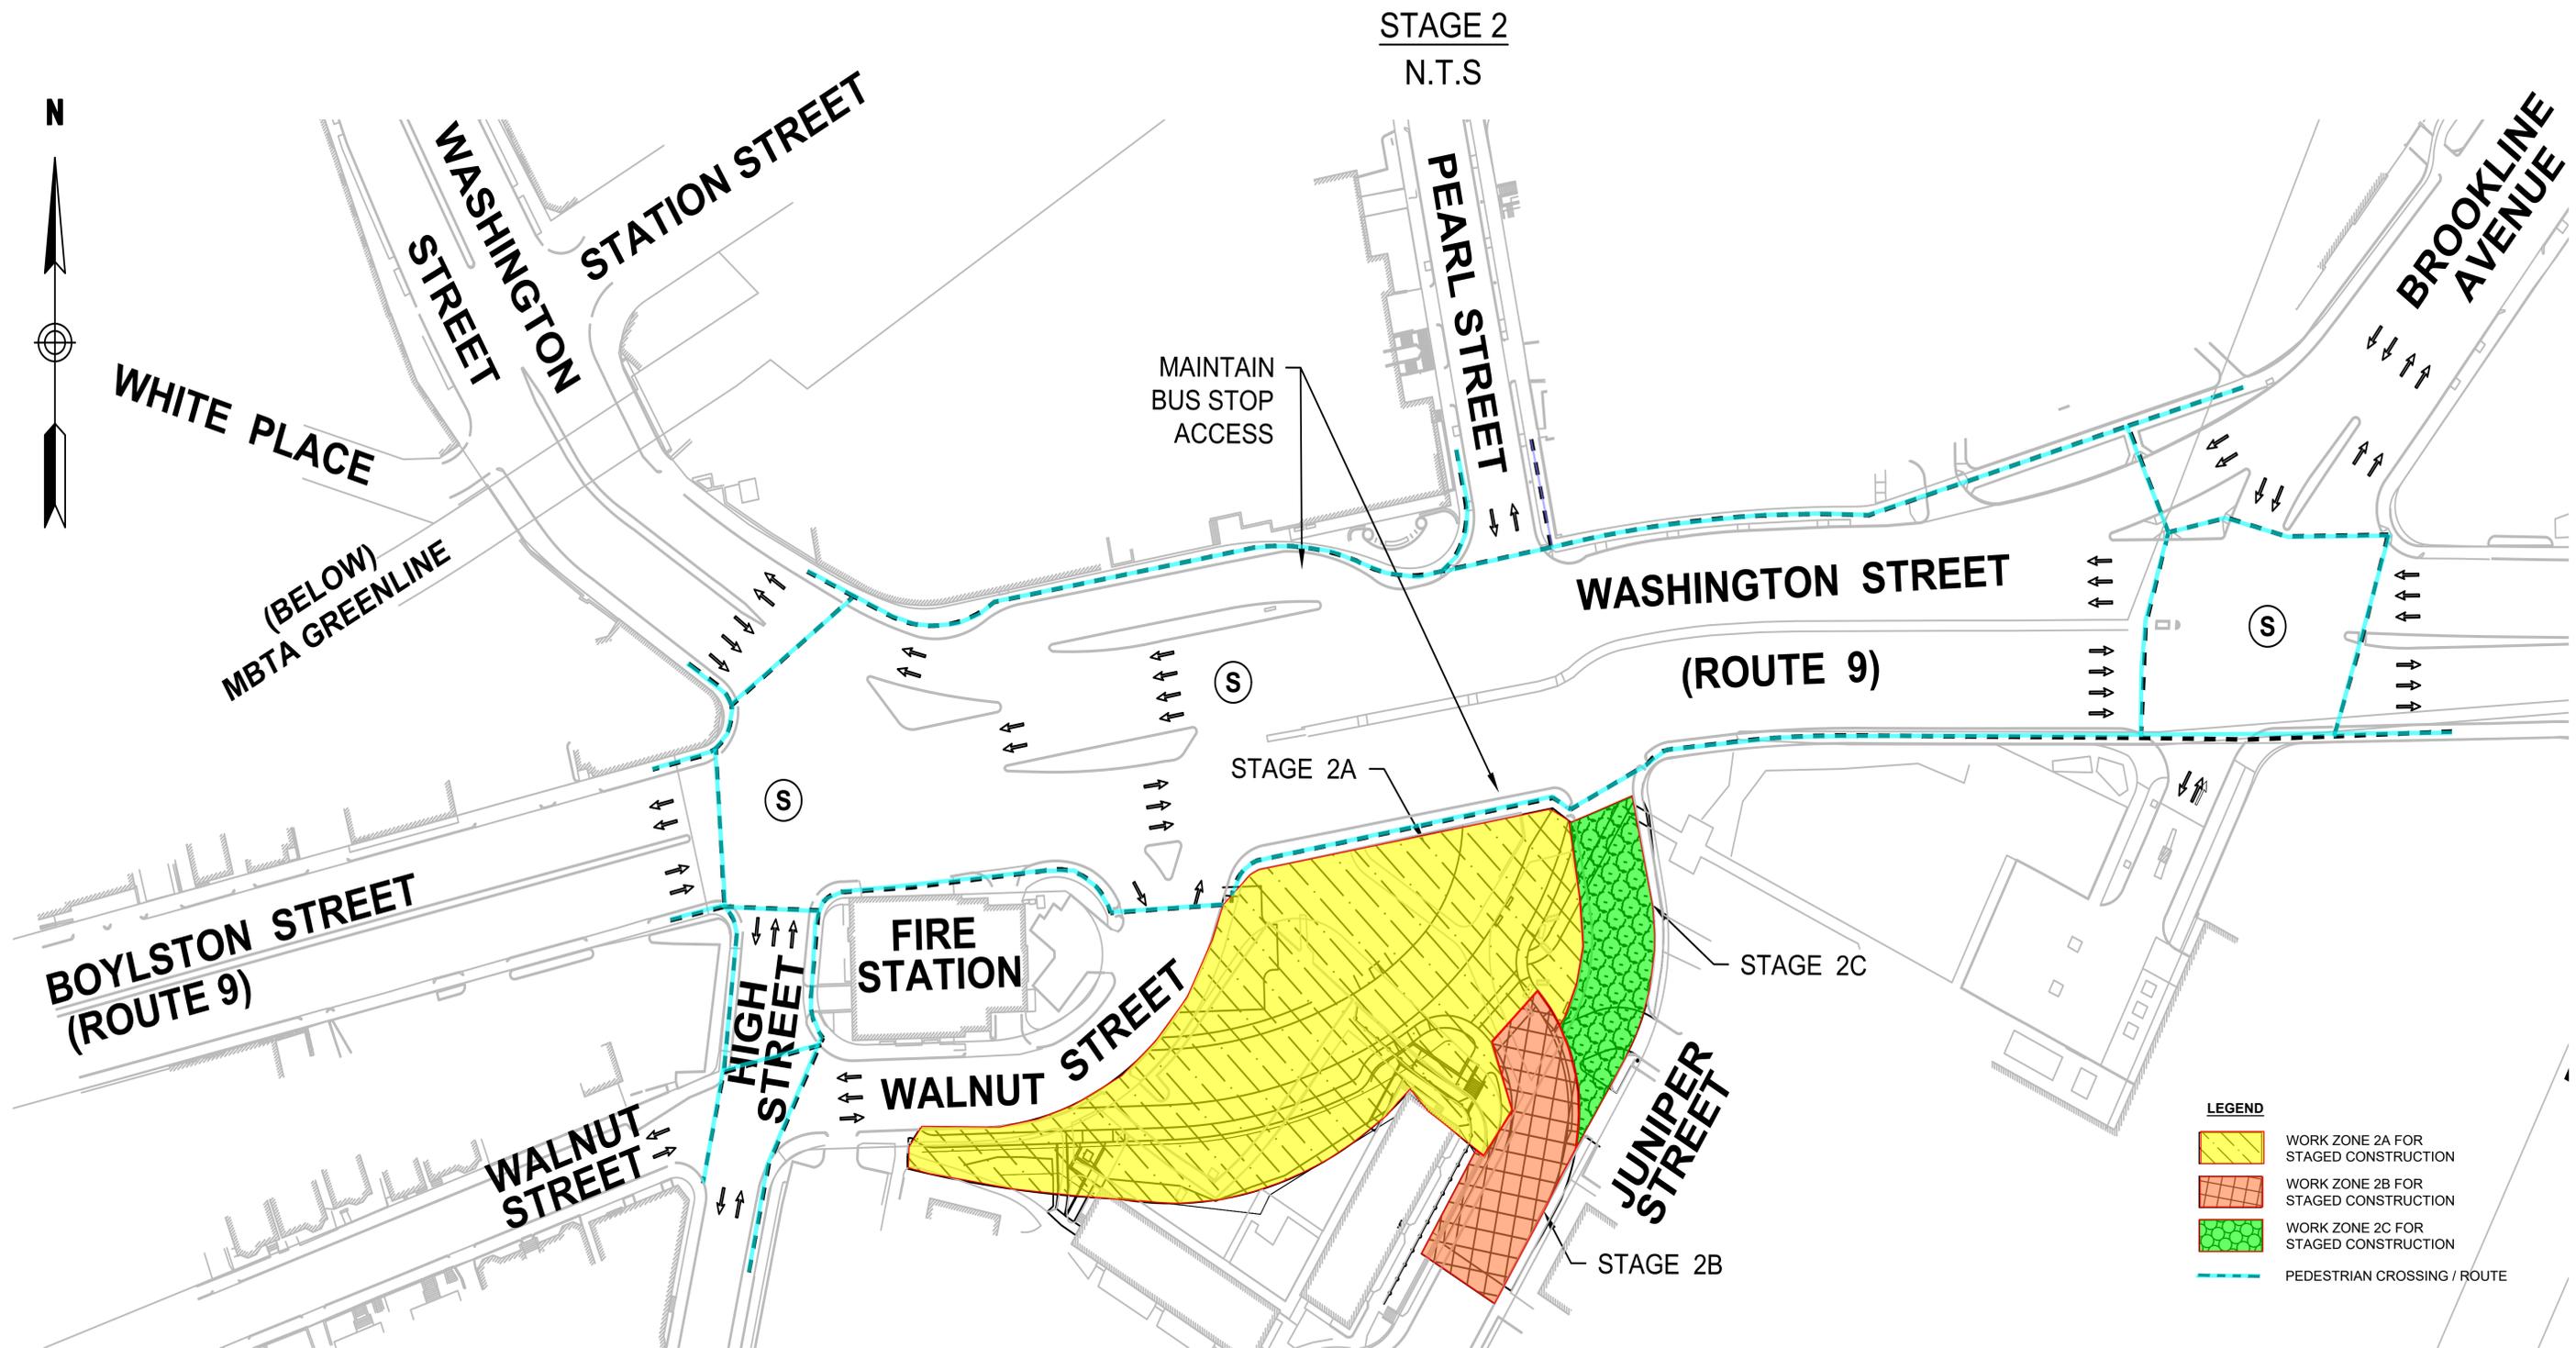

**\*Walnut Street & Juniper Street to Remain open and unchanged during phase 2A construction\***
