



TOWN OF BROOKLINE


Massachusetts

DEPARTMENT OF PUBLIC WORKS Engineering & Transportation Division

December 1, 2011

Andrew M. Pappastergion
Commissioner
Peter M. Ditto, PE
Director

DECEMBER LOOK-AHEAD at Sewer Separation Project Activities:

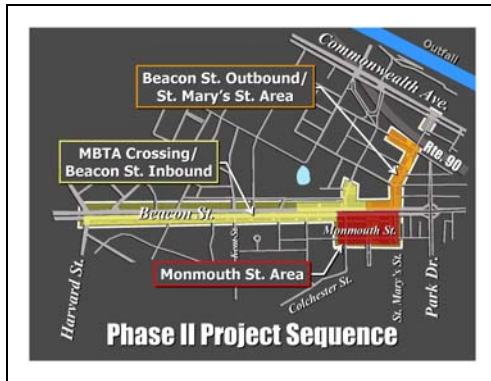

- (A) **ST. MARY'S STREET AREA (Beacon north to Mountfort)**
December Work: Access pits closed and No Work Scheduled through winter
Traffic/Parking: Two-way Traffic and Parking Restored
- (B) **BEACON STREET (outbound) COMMERCIAL/RESIDENTIAL AREA**
December Work: Early-Dec, demobilize drilling equipment at Beacon approach to Carlton; Relocate all equipment to Beacon (inbound) between St. Paul and Marshal; Mid-Dec, complete installation of concrete interceptor and manhole structures at access pits in front of 1038 and 1054 Beacon; End-Dec, backfill both access pits and provide asphalt surface for winter months
Traffic/Parking: Single lane westbound during work hours (Mon-Fri, 7AM-5PM) pending end-Dec closure of pits; Intermittent delays during demobilization; Curbside parking restricted only adjacent access pits; Median parking open between St. Mary's and Carlton; however, early-Dec short-term restriction designates +/-8 median spaces west of Carlton for pipe staging
- (C) **BEACON STREET (inbound) COMMERCIAL/RESIDENTIAL AREA**
December Work: Early-Dec backfill/resurface Carlton pit; Early-Dec complete 42" drain installation through St. Mary's intersection; Early-Dec mobilize and stage pipe in vicinity of St. Paul pit for mid-Dec launch of drilling operation/pipe compression from St. Paul pit west to Kent; End-Dec install manhole structures and backfill/resurface pits at Kent and St. Paul; Mid-Dec install Borland manhole structure and sewer tie; End-Dec backfill/resurface Borland pit
Traffic/Parking: Early-Dec restore curbside parking and 2-travel lanes from Hawes to St. Mary's; Through end-Dec, single lane eastbound from St. Paul to Borland, and Curbside parking restricted adjacent work sites at St. Paul, Kent and Borland; End-Dec re-open Borland St and curbside parking
- (D) **MONMOUTH STREET AREA (St. Mary's west to Carlton)**
December Work: Early-Dec restore Catch Basin/resurface Monmouth roadway/sidewalk for winter; Early-Dec St. Mary's (Monmouth to Beacon) is a staging area pending completion of Beacon drain
Traffic/Parking: Early-Dec restore vehicular circulation/parking; Intermittent Detours from Beacon
- (E) **CARLTON STREET CORRIDOR (Monmouth north through Beacon)**
December Work: Early Dec at Beacon, demobilize and relocate tunneling equipment to St. Paul
Traffic/Parking: Early to mid-Dec, intermittent construction delays at Beacon intersection

Project Web Site: www.brooklinema.gov

From Brookline Homepage navigate to 'News & Update' menu for DPW Sewer Separation Project
Telephone: (617) 730-2139 for Bill Smith --or-- Email: wsmith@brooklinema.gov
